



**JURUPA ROAD**  
GRADE SEPARATION



City of Jurupa Valley

John Ashlock, PE  
Division Manager – Construction  
County of Riverside Transportation Department

June 5, 2025





# JURUPA ROAD

## GRADE SEPARATION

## AGENDA

- Project Overview
- Project Update
- Path To Completion





# JURUPA ROAD

## GRADE SEPARATION

## Project Overview

The Jurupa Road Grade Separation project will separate train traffic from vehicles, pedestrians and cyclists by constructing an underpass under Van Buren Blvd. and the UPPR tracks.





## Project Cost

### Initial Project Cost

- \$133.4 million total

### Current Project Cost

- \$184 million total

The additional project costs are a result of the following:

- Increased cost of labor and materials
- New design requirements by UPRR
- Delay in project timeline related to C&M agreement



# JURUPA ROAD

## GRADE SEPARATION

## Project Overview Timeline

- October 2017 - City Agreement / Funding Co-op executed
- December 2020 - Final civil design completed
- July 2021 - Contract awarded to Granite Construction
- July 2021 - Construction began
- January 2024 - Final UPRR plans and Construction and Maintenance (C&M) agreement completed



# JURUPA ROAD

## GRADE SEPARATION



# JURUPA ROAD

## GRADE SEPARATION

## Milestones

- July 2021 - Construction began
- January 2022 - Jurupa Road closed
- January 2022 - Jurupa Connector Road opened
- July 2022 - Contractor began railroad pre-fabrication off-site





# JURUPA ROAD

## GRADE SEPARATION

## Milestones

- January 2024 - 1,500 linear feet of reinforced concrete box drainage completed
- August 2024 - 660 feet of concrete retaining walls completed on Jurupa Road Underpass
- August 2024 - Pump Station structures substantially completed, finish work to be done at end of project



# JURUPA ROAD

## GRADE SEPARATION





# JURUPA ROAD

## GRADE SEPARATION

## Milestones


- Early 2024—Intersection improvements at Van Buren Blvd. and Rutile St. completed
- Anticipated July 2025 - Pedley Road and Jurupa Road intersection improvements completed



# JURUPA ROAD

## GRADE SEPARATION

### Construction Activities

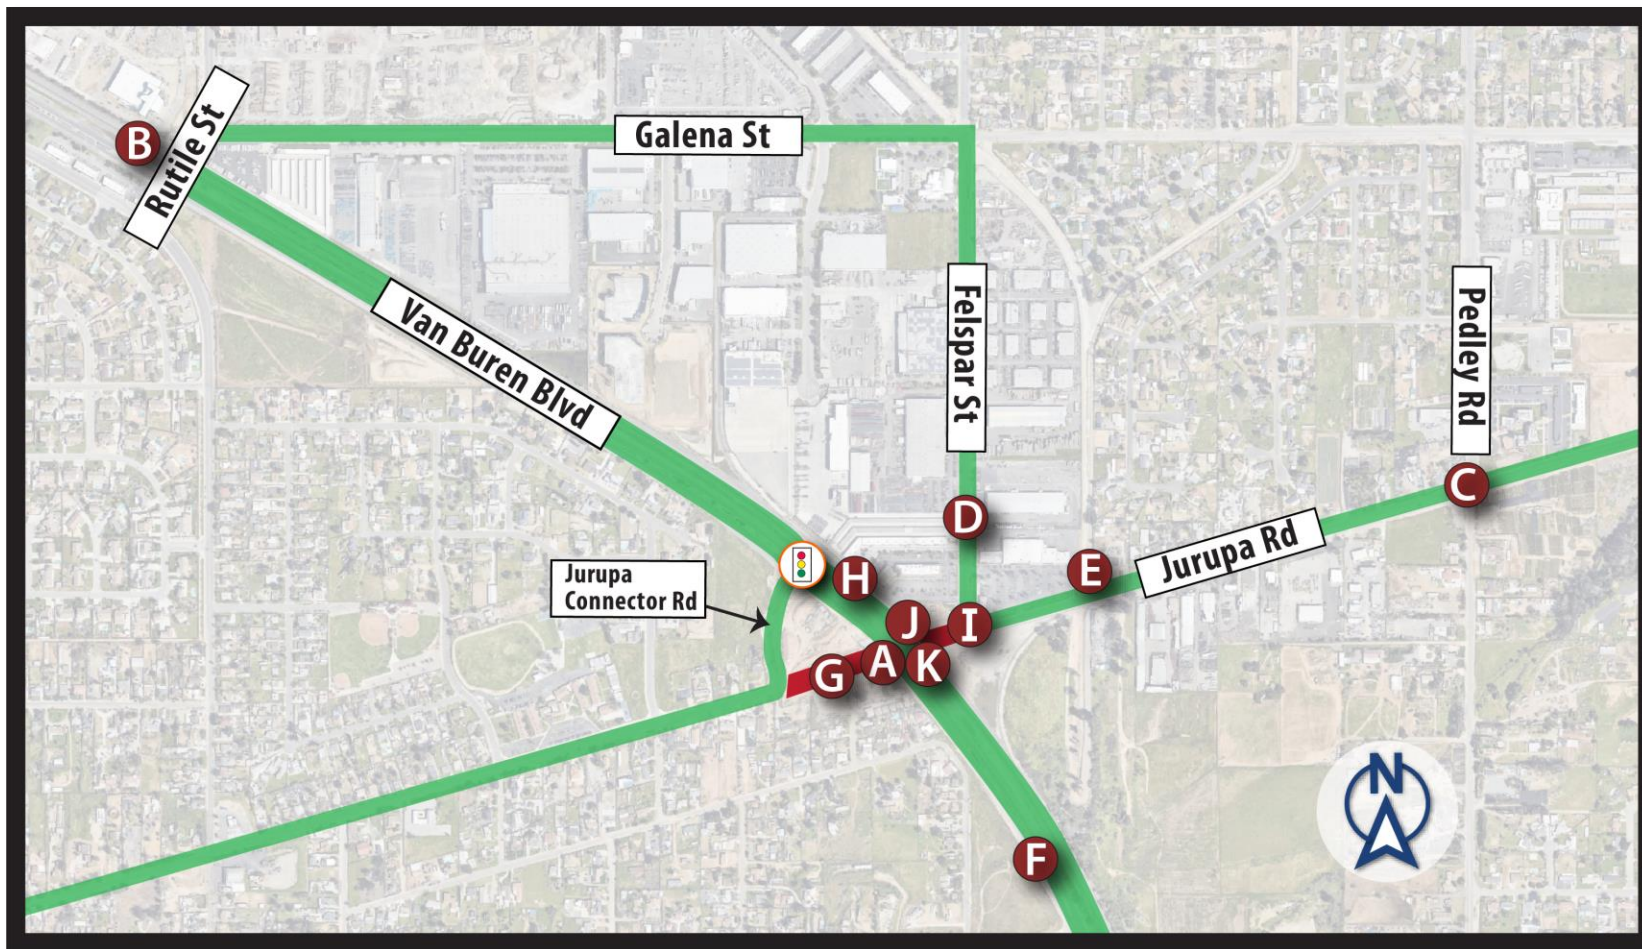



## **Project Impacts**

- Impacts from Covid and difficulty in securing materials
- Utility relocation coordination
- UPRR Construction and Maintenance agreement
- Work planning and safety coordination with the project team and UPRR



## Path to Completion

1. Railroad Track

- Continue to construct temporary railroad track and switch trains
- Construct permanent track

2. Construct UPRR Bridge

3. Construct Northbound Van Buren Blvd. Bridge

4. Construct Jurupa Road Undercrossing


5. Project Completion: Late 2027



# JURUPA ROAD

## GRADE SEPARATION

## Updated Project Timeline

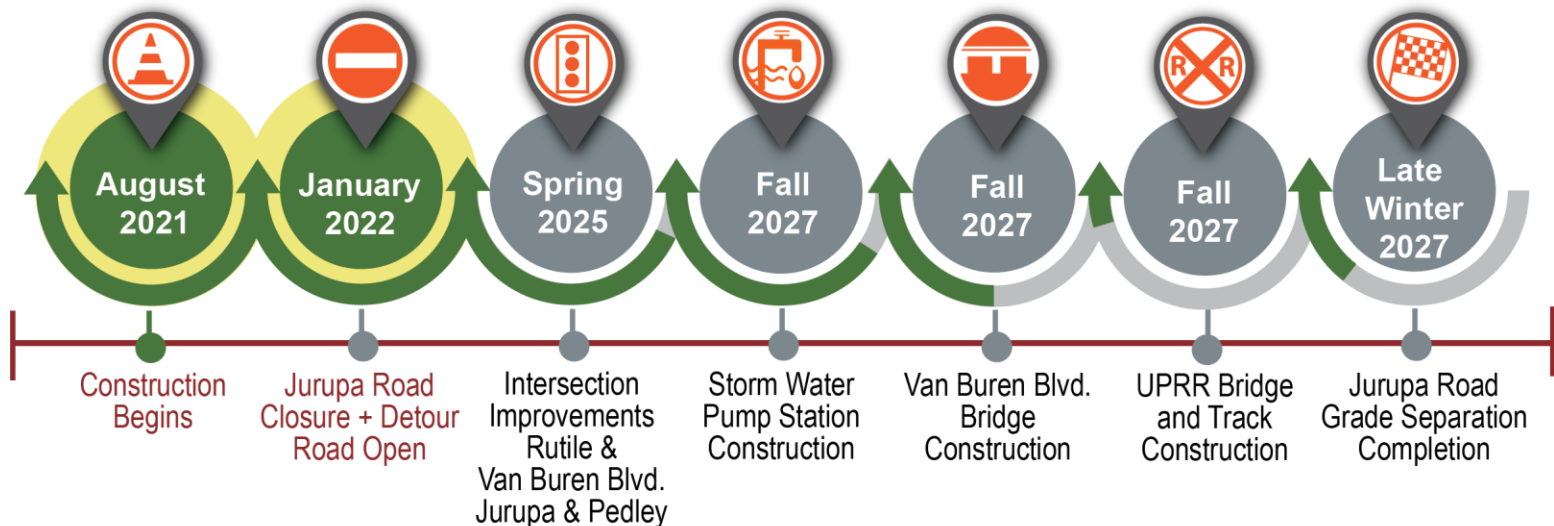



# JURUPA ROAD

## GRADE SEPARATION



**[JurupaGradeSeparation.com](http://JurupaGradeSeparation.com)**  
**Construction Hotline: 800-679-9570**

### Project Partners



# JURUPA ROAD

## GRADE SEPARATION

# QUESTIONS?




### Project Partners



# JURUPA ROAD

## GRADE SEPARATION

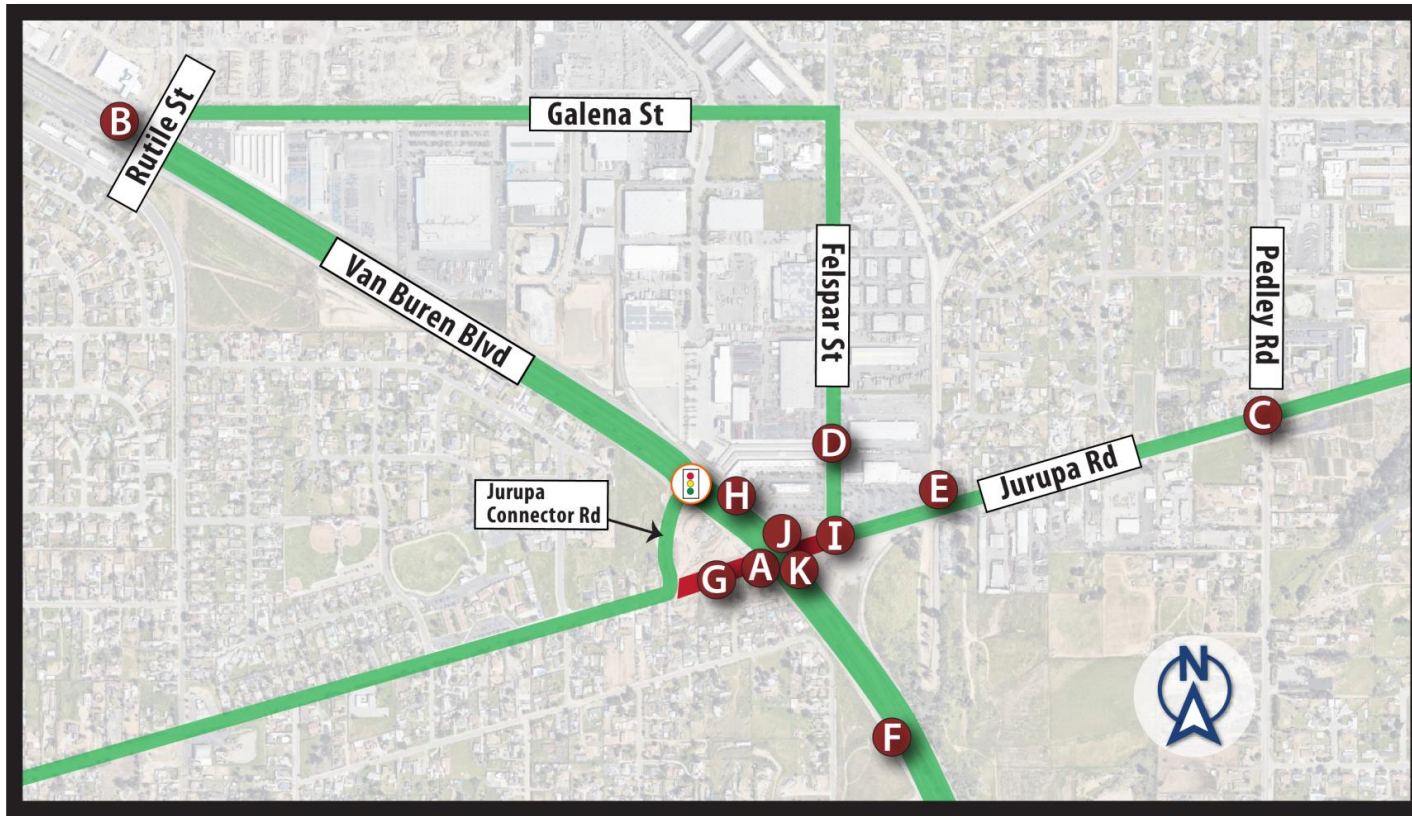

### Project Partners

