



**JURUPA ROAD**  
GRADE SEPARATION



City of Jurupa Valley

John Ashlock, PE  
Division Manager – Construction  
County of Riverside Transportation Department

March 5, 2026





# JURUPA ROAD

## GRADE SEPARATION

## AGENDA

- Project Overview
- Project Update Since October 2025
- Path To Completion



# JURUPA ROAD

## GRADE SEPARATION

## Project Overview

The Jurupa Road Grade Separation project separates train traffic from vehicles, pedestrians and cyclists by constructing an underpass under Van Buren Blvd. and the UPPR tracks.



# JURUPA ROAD

## GRADE SEPARATION

### Project Update

Temporary Track Installation **100%** complete.

Trains switched over in early November 2025



# JURUPA ROAD

## GRADE SEPARATION

Completed punch list activities at the intersection of Jurupa and Pedley roads including:

- Lowered traffic signal heads
- Concrete curb and handrailing modifications
- Striping



# JURUPA ROAD

## GRADE SEPARATION

Completed excavation and shoring for the UPRR bridge –  
January 2026.



# JURUPA ROAD

## GRADE SEPARATION

### In Progress

Construction on the UPRR bridge over Jurupa Road began in January 2026. Expected completion is Fall 2027.





# JURUPA ROAD

## GRADE SEPARATION

## In Progress

Grading started for the permanent railroad track in January 2026.

Track construction planned to begin in March 2026.

Permanent track completion expected late in 2026.



# JURUPA ROAD

## GRADE SEPARATION

## Upcoming


Jurupa Road construction east of Felspar Street set to begin in Spring 2026.  
Jurupa Road and Felspar Street will fully open at the end of the project in late 2027.



# JURUPA ROAD

## GRADE SEPARATION

### Construction Activities

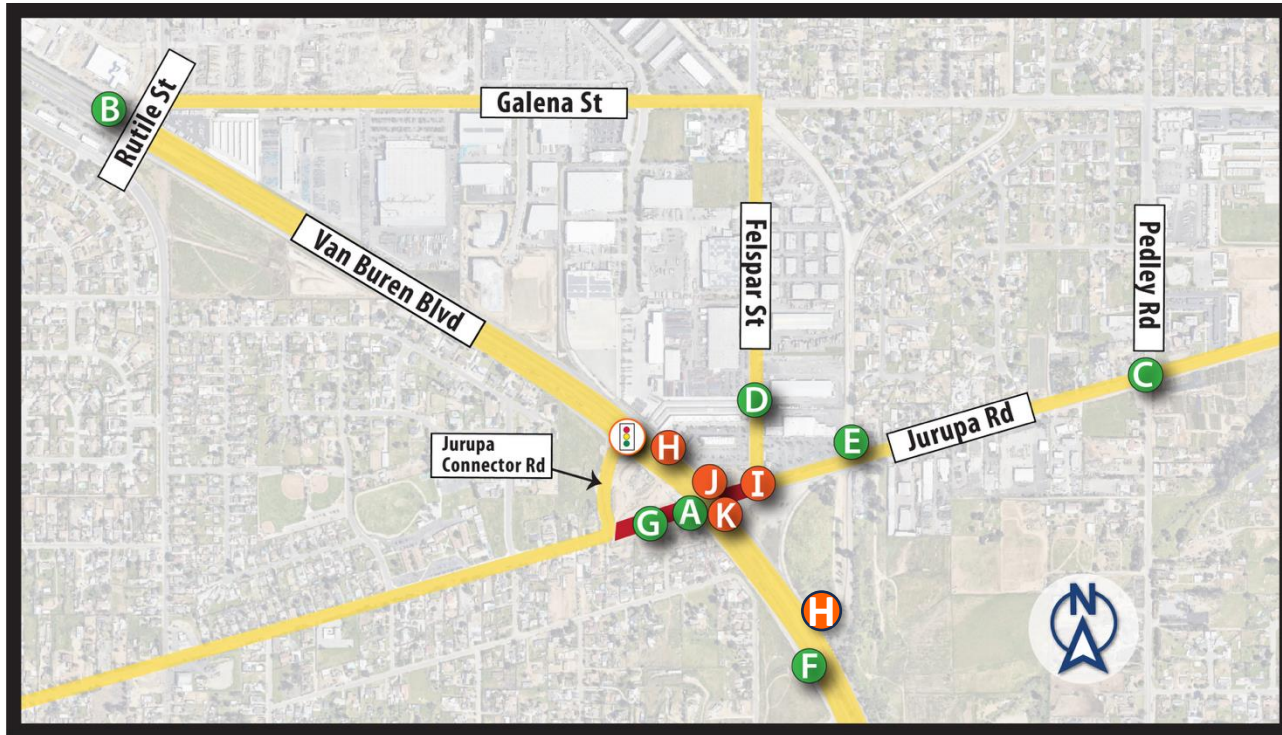

**H** Permanent railroad track under construction

**J** UPRR Bridge Stage 1 under construction

**K** Stage 2 construction on UPRR and Van Buren bridges expected to start early 2027

**I** Construct Jurupa Road Undercrossing and open Jurupa & Felspar intersection – expected completion late 2027



# JURUPA ROAD

## GRADE SEPARATION

## Path to Completion


1. Stage 1 UPRR bridge – expected completion Fall 2026
2. Railroad Track
  - Construct permanent track – expected completion late 2026
3. Construct Stage 2 UPRR and Van Buren Blvd. bridges – expected to start early 2027
4. Construct Jurupa Road Undercrossing and open Jurupa & Felspar intersection – at project completion late 2027



# JURUPA ROAD

## GRADE SEPARATION

### Updated Project Timeline

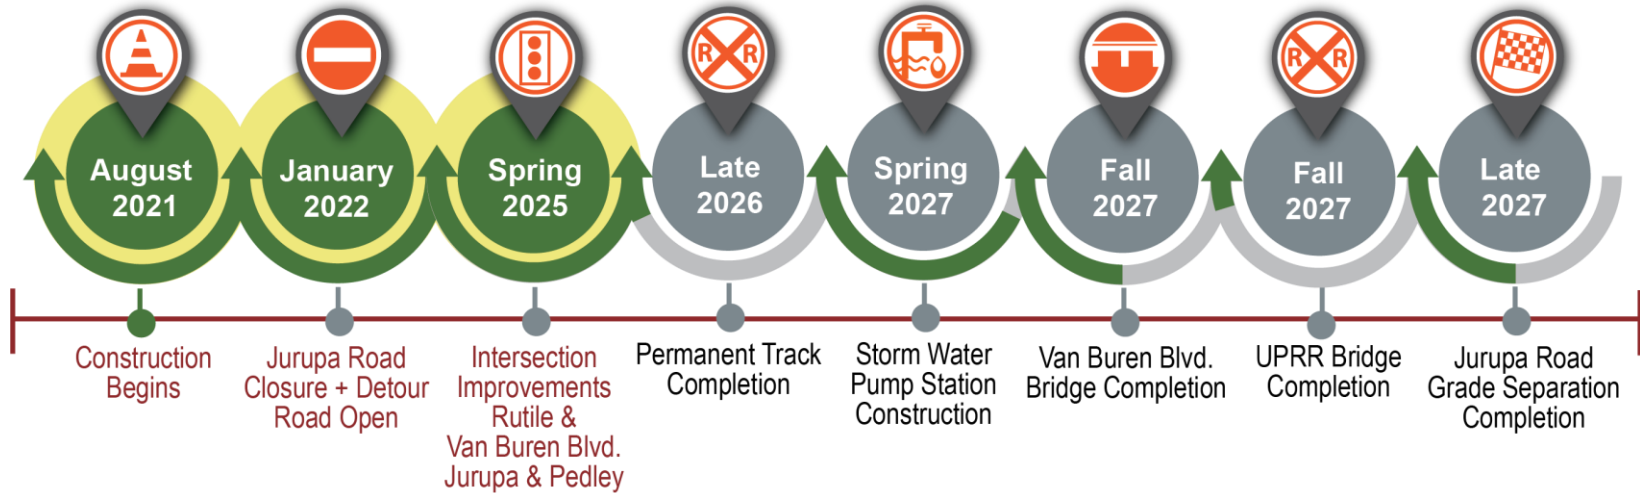



# JURUPA ROAD

## GRADE SEPARATION

## Community Outreach Update

1. Ongoing coordination with city and stakeholders.
2. Provide timely project notifications and updates to stakeholders, residents, businesses, and the community.
3. Continue email communication and monthly in-person visits to businesses in the project area.



# JURUPA ROAD

## GRADE SEPARATION

### Community Outreach Update

#### Paid Social Media Campaign

Nov. 2025 – Jan. 2026

Total Meta Ad Spend: **\$2,000**

- Reached **127,050 residents**
- Generated **58,594 engagements**
- Drove **5,141 website link clicks**
- **4,290 sessions** on the project updates webpage received
- **118 new contacts** added to email list



[www.jurupagradeseparation.com](http://www.jurupagradeseparation.com)



@JurupaGradeSeparation



@JurupaGradeSeparation

The collage features three social media advertisements. The top ad is a video titled "TIS THE SEASON SHOP LOCAL BE MERRY" with the hashtag #SHOPLOCAL JURUPA VALLEY. The middle ad is a video titled "Know what's coming before your commute! Sign up for project alerts to receive updates on closures, detours, and construction". The bottom ad is a video titled "February is the perfect time to show a little love" and includes a "SIGN UP FOR ALERTS PLAN YOUR COMMUTE" button and a "BUSINESSES OPEN" badge. The collage also includes a heart-shaped graphic filled with photos of local businesses and a screenshot of a social media post from "jurupagradeseparation" showing engagement metrics.



# JURUPA ROAD

## GRADE SEPARATION



**[JurupaGradeSeparation.com](http://JurupaGradeSeparation.com)**  
**Construction Hotline: 800-679-9570**

### Project Partners

