



JURUPA ROAD
GRADE SEPARATION



City of Jurupa Valley

John Ashlock, PE
Division Manager – Construction
County of Riverside Transportation Department

October 2, 2025





JURUPA ROAD

GRADE SEPARATION

AGENDA

- Project Overview
- Project Update Since June 2025
- Path To Completion





JURUPA ROAD

GRADE SEPARATION

Project Overview

The Jurupa Road Grade Separation project will separate train traffic from vehicles, pedestrians and cyclists by constructing an underpass under Van Buren Blvd. and the UPPR tracks.





JURUPA ROAD

GRADE SEPARATION

Project Overview

Architectural rendering of the completed project; not to scale.



JURUPA ROAD

GRADE SEPARATION

Bly Channel Extension, **95%** complete



JURUPA ROAD

GRADE SEPARATION

Arch Culvert Drainage Improvements **100%** complete



JURUPA ROAD

GRADE SEPARATION

Intersection Improvements and Traffic Signal Installation at Jurupa and Pedley Roads **100%** complete



JURUPA ROAD

GRADE SEPARATION

- Stormwater Pipe Installation **95%** complete on Felspar Street and behind plazas
- Curb, gutter, and sidewalk construction; paving on Felspar Street **90%** complete



JURUPA ROAD

GRADE SEPARATION


Temporary Track Installation **70%** complete; expected completion and Train Switchover — December 2025



JURUPA ROAD

GRADE SEPARATION

Construction Activities

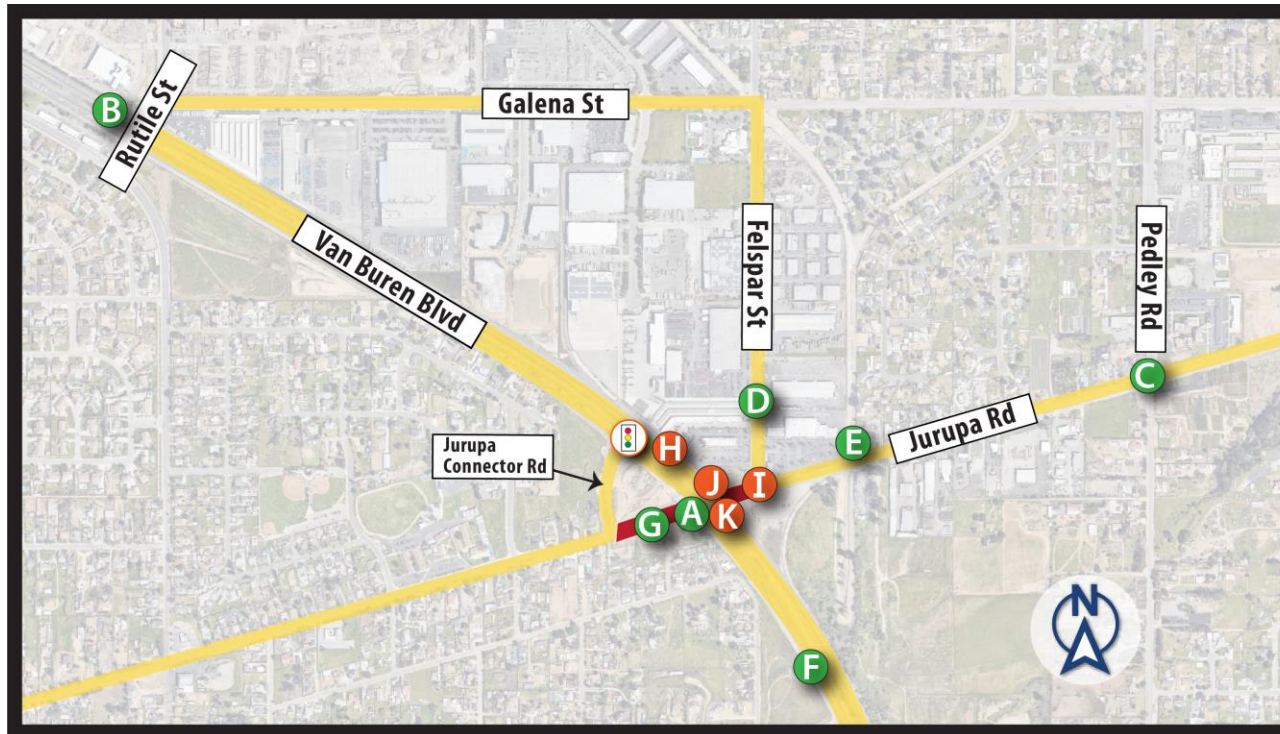

H Railroad track under construction

J Phase 1 construction on UPRR Bridge expected to start Spring 2026

K Phase 2 construction on UPRR and Van Buren bridges expected to start Winter 2026

I Construct Jurupa Road Undercrossing and open Jurupa & Felspar intersection – expected completion Winter 2027



JURUPA ROAD

GRADE SEPARATION

Path to Completion


1. Railroad Track
 - Complete temporary railroad track and switch trains – Winter 2025
 - Construct permanent track – expected to start Winter 2026
2. Construct Phase 1 UPRR bridge – expected to start Spring 2026
3. Construct Phase 2 UPRR and Van Buren Blvd. bridges – expected to start Winter 2026
4. Construct Jurupa Road Undercrossing and open Jurupa & Felspar intersection – project completion Winter 2027



JURUPA ROAD

GRADE SEPARATION

Updated Project Timeline

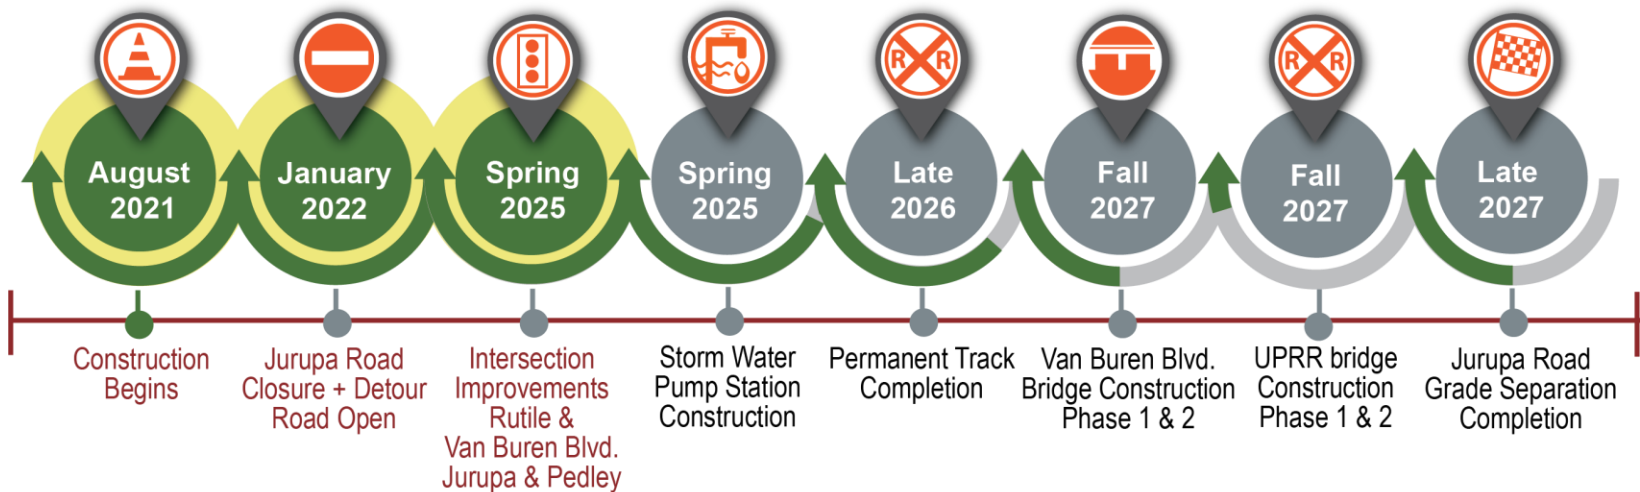



JURUPA ROAD

GRADE SEPARATION

Community Outreach Update

1. Provide timely project notifications and updates to stakeholders, residents, businesses, and the community.
 - 443 email/text contacts; 23 stakeholders
2. Added banners in shopping plaza and on flood control fencing at Felspar and Galena streets as requested by businesses.
3. Coordinate outreach with city and continue to provide weekly updates, photos and social media posts.
4. Continue outreach and monthly in-person visits to businesses in the Felspar Street shopping plazas.





JURUPA ROAD

GRADE SEPARATION

Community Outreach Update

5. Social media advertising month-long trial campaign in June 2025 delivered strong awareness and targeted community engagement.
- **16,000** people reached
 - **7,200** video views
 - **4,400** interactions
 - **139 new website visitors** during campaign, an increase of 6.1%, of which 96% were first-time visitors

www.jurupagradeseparation.com

 Instagram @JurupaGradeSeparation

 Facebook @JurupaGradeSeparation





JURUPA ROAD

GRADE SEPARATION



JurupaGradeSeparation.com
Construction Hotline: 800-679-9570

Project Partners

